

Food Delivery App Launch Charter

With society turning into a more digitalized place more and more restaurants and grocery stores are also adding a delivery app to their business process. This project focuses on the planning, design, development and launching of a mobile food delivery application for a startup business within a period of three months. The purpose of the project is to create a digital platform that connects customers, restaurants, and delivery drivers through a fast, convenient and user-friendly mobile application.

The objectives of the project are:

- to create a simple, fast, and user-friendly food ordering experience for customers while helping restaurants increase online sales.

1. Project Scope

Included:

- Customer registration and login
- Restaurant listing
- Food menu browsing
- Cart functionality
- Online payment integration
- GPS delivery tracking
- Push notifications
- Order history
- Admin dashboard
- Restaurant management dashboard
- Mobile responsive interface

Excluded:

- Delivery drivers
- International food delivery
- Cryptocurrency payments
- Third-party logistics company integration

Scope Boundary:

The project focuses only on building and launching the food delivery application within the local market. The scope is limited to mobile application functionality, ordering systems, payment processing, and delivery tracking.

The project does not include:

- Expansion into multiple countries
- Hardware delivery systems
- Restaurant kitchen management systems

Scope Creep Control:

To prevent scope creep:


- All feature requests must be approved by the project manager
- New features after development begins require formal change requests
- The development team will follow approved requirements only
- Timeline and budget changes require stakeholder approval

2. Expected Launch Timeline

This project will be completed over a period of 90 days (3 months)

Phase	Duration	Milestone
Project Initiation	Day 1 - Day 7	Project charter approved
Requirements Gathering	Day 8 - Day 17	Requirements finalized
UI/UX Design	Day 18 - Day 30	App design completed
Development	Day 31 - Day 60	Core features developed
Testing	Day 61 - Day 75	Bugs fixed and system validated
Deployment & launch preparation	Day 76 - Day 85	App deployed to stores
Marketing & launch	Day 86 - Day 90	Official app launch

Gantt Chart

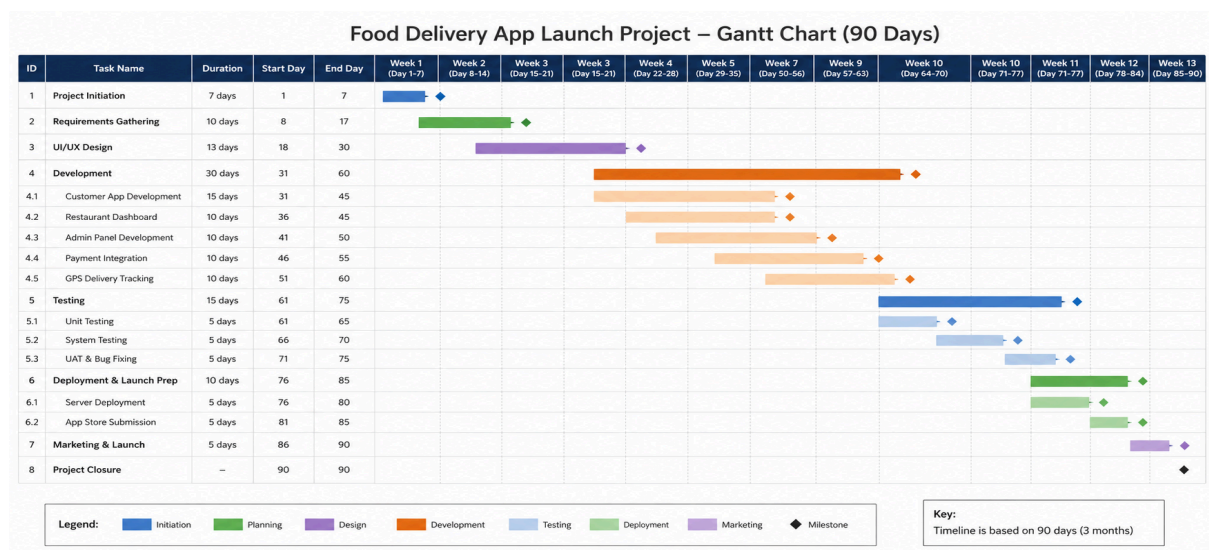

3. Work Breakdown Structure(WBS)

1. Project Initiation

- Create project charter
- Identify stakeholders
- Define project objectives
- Gather business requirements

2. System Analysis & Design

- Analyze competitor apps
- Create process flow diagrams
- Design wireframes and UI mockups
- Define the database structure

3. Application Development

- Develop the customer mobile app
- Develop the restaurant dashboard
- Develop the admin panel
- Integrate the payment gateway
- Integrate GPS delivery tracking

4. Testing

- Unit testing
- System testing
- Mobile responsiveness testing
- Payment testing
- Bug fixing

5. Deployment

- Deploy backend server
- Publish app to Google Play Store
- Publish app to Apple App Store

6. Marketing & Launch

- Social media marketing
- Influencer promotions
- Customer onboarding campaigns

7. Documentation & Closure

- Prepare user guides
- Final project report
- Project closure

4. Project Charter

Project Charter

Title	Food delivery Application
Start Date	01 June 2026
End Date	30 August 2026
Project Manager	Buhle Mduli
Overview	Create a simple, fast, and user-friendly food ordering experience for customers while helping restaurants increase online sales.
Scope	The project focuses only on building and launching the food delivery application within the local market. The scope is limited to mobile application functionality, ordering systems, payment processing, and delivery tracking.
Budget and Resources	Financial Resources : Total Estimate Cost is R135 000 Technical Resources : Includes laptops, Mobile testing devices, Cloud hosting server, Database Management system, Payment Gateway API, GPS API, Development Human Resources : Includes Project manager, Business analyst, UI/UX Designer, Frontend Developers, Backend Developers, Database Administrator, QA tester, Marketing Team, IT Support
Stakeholders	Food Delivery app owners, Project Manger, Business Analyst, UI/UX Designer, Developers, Tester/QA Team, Resturants, Delivery Drivers, Customers
Success Criteria	1.Application launched on time 2.System functionality 3.User-friendly interface 4.Payment intergration works sucessfully 5.Delivery tracking operates correctly 6.Mobile responsiveness 7.System perfomance 8.Security compliance 9.Resturant onboarding completed 10.Customer satisfaction
Methodology	Agile Methodology
Approvals	Following stakeholders : Food Delivery app owners, Project Manger, Business Analyst, UI/UX Designer, Developers, Tester/QA Team

5. Resource Plan

Human Resources:

- Project Manager - Oversees project activities
- Business Analyst - Gathers and documents requirements
- UI/UX Designer - Designs user interface
- Frontend Developers - Build mobile app screens
- Backend Developers - Build APIs and database
- Database Administrator - Manages database
- QA Tester - Tests application
- Marketing Team - Promotes app launch
- IT Support - Handles technical support

Technical Resources:

- Laptops/Computers - Development work
- Mobile testing devices - App testing
- Cloud hosting server - Application hosting
- Database Management System - Data storage
- Payment Gateway API - Online payments
- GPS API - Delivery tracking
- Development Software - Coding and deployment

Financial resources:

Item	Estimated Cost
UI/UX Design	15 000
Mobile App Development	40 000
Backend Development	30 000
Testing & QA	20 000
Hosting & Server Costs	8 000
Marketing Campaign	12 000
App Store Publishing Fees	5 000
Miscellaneous Costs	5 000
Total Estimated Cost	135 000

Project Constraints

There are several challenges that may affect the availability and use of resources in the this project and they may include:

- Time - The project must launch within 3 months
- Budget - Startup businesses usually have limited funding
- Resources - A small development team
- Technology - The app must support Android and iOS
- Compliance - The app must comply with payment security standards

Project Assumptions

- Developers and designers will be available throughout the project
- Internet access will be stable during development
- Restaurants will cooperate during onboarding
- Payment gateway approval will be completed on time
- Customers will use smartphones to access the app

6. Milestone and Launch plan

Milestone	Target Date
Project Approval	Day 7
Requirements Completed	Day 17
UI/UX Design Approved	Day 30
Development Completed	Day 60
Testing Completed	Day 75
App Published to Stores	Day 85
Official Launch	Day 90

Launch Strategy

The launch strategy will include:

- Social media advertising
- Restaurant partnership promotions
- Discount codes for first-time users
- Influencer marketing
- Time-limited promotional offers

Conclusion

The Food Delivery App Launch Project aims to provide a modern and efficient digital food ordering platform within a 3-month timeline. By carefully managing scope, resources, risks, and milestones, the startup can successfully launch a user-friendly application that improves customer convenience and supports restaurant growth.
